

Green Lanes Construction

Progress update

12 March 2014

St Ann's Junction Construction
06 JAN 14 to 22 MAY 2014

Raised Carriageway Table Construction
Temporary Traffic Signals (2 nights)
5th - 6th May

Green Lanes Construction Status



11 March 2014



Current construction



Approaching construction
(within 2 weeks of the above date)



Completed construction



Pending construction



Road closure during raised table installation
(access will be allowed)

TBC*
To be programmed on completion of The
Gardens Community Streets speed table
construction programme



The text below is a standard supplemental to the programme of works shown on the previous page that forms the bi-monthly update regarding construction progress.


Please note:

Bays shown in green are bays that have substantial disruptive works completed; there will still be further less disruptive works required to be undertaken to finalise these bays – **this will include installation of street furniture i.e. benches, cycle stands, signs / posts etc.**

Streets will be required to be temporarily closed (access still allowed) for the installation of the raised carriageway sections at junctions - this document will give advance notice of these works. Affected addresses will also receive a posted notification in advance of the closures. The closures for The Gardens streets will follow the works currently being undertaken for The Gardens Community Streets scheme.

1. Shop deliveries - Loading / Unloading

Haringey Council will be temporarily suspending parking at the Green Lanes end of each street adjacent to each Bay of active construction (example illustration below). This is to provide our construction contractor with a required area for works purposes. Both sides of the street directly adjacent to the live construction Bay will be suspended; and a section of the suspended parking bays will be temporarily allocated specifically for business loading purposes (shown in green).

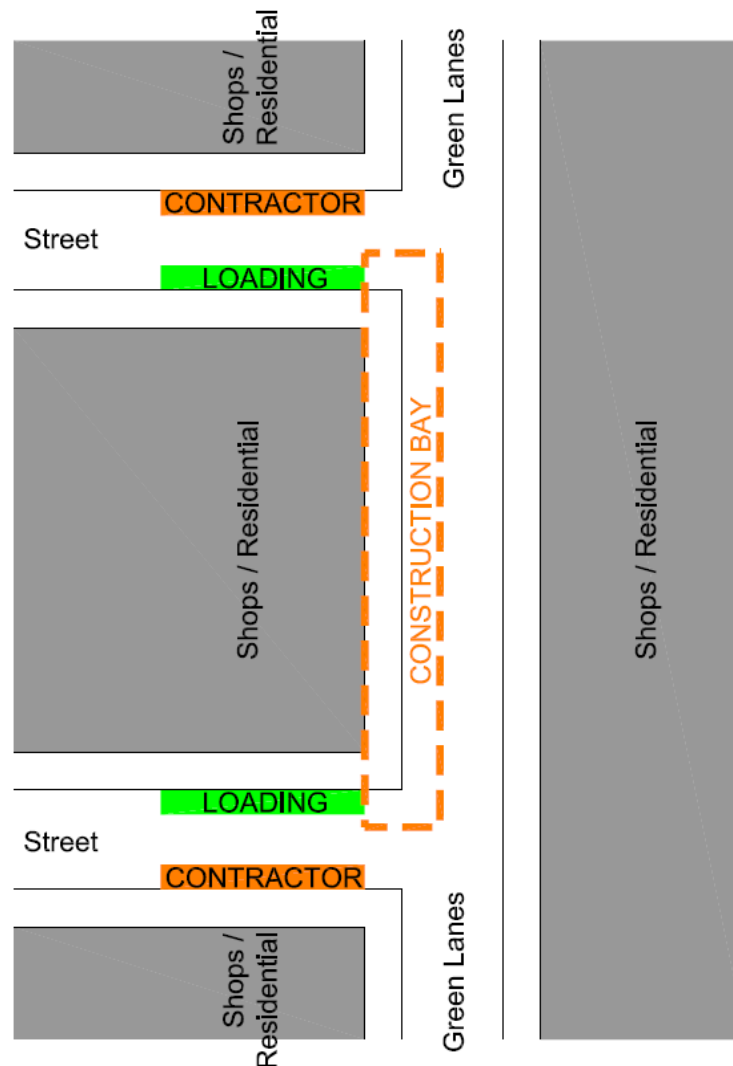

2. Strategy for waste management

Residential waste is usually deposited on the footway on Green Lanes and at present our contractor has provided gangways to each doorway (business and resident) to allow entry/exit from premises. Residents should leave their waste at the carriageway end of these gangways (on the footway, within and near to the barriers), which will allow rubbish to be collected as usual.

Businesses with their own individual contracts for waste disposal will need to inform their contractor of construction to allow preparation for their continued management of waste disposal.

If you have any enquiries regarding waste collection, Veolia can be contacted on their general enquiries number: 020 8885 7700.

3. Provision of access to shops/businesses/restaurants/residential

There will be disruption during the construction period, which we will try our best to keep to a minimum. Access to business will be maintained for the majority of the construction period, but there will be short durations when access will be fully blocked. Our contractor will individually liaise with properties to agree the most convenient time for this to occur.

4. Disabled access

Access will be maintained to residences/ businesses. A minimum width of walkway of 1.2m will be maintained at all times.

5. Working Hours

General operations

Standard: Monday to Friday - 08:00 to 18:00

Saturday: 08:00 to 13:00

Sunday: None

Allowable out of hours works

Construction work may be undertaken outside of the hours shown above, only if the works do not affect traffic flows and are quiet works such as site clearance or material deliveries.

Working hours constraints

No construction works will be undertaken during the Christmas Embargo, which is from 2 December 2013 to 5 January 2014.
